




Project Management | OOTB Introduction

Your Guides

Mindy Calderon And Dakota Brown


Project Management - OBS

- The OBS is a hierarchical structure that outlines the framework of the organization.
- Projects, Ideas, and Resources are 'attached' to the appropriate level in the OBS.
- The association of Resources and Projects to the OBS allows for:
 - Targeting of specific areas within the organization to filter and report on data
 - Clarity PPM access level rights

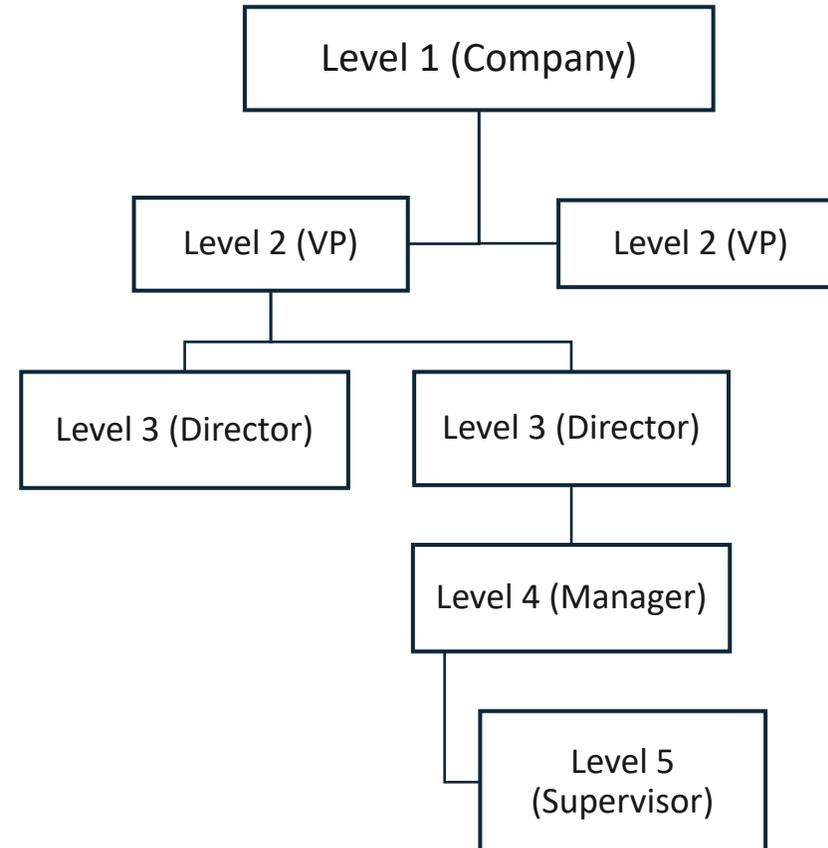

Project Management - WBS

- *WBS typically consists of phases, activities, and tasks.*
 - Phases are the major steps required to achieve a project goal.
 - Activities are established to complete the phase objectives.
 - Activities are split into tasks to break up the work.
 - Milestones have no duration and no work effort.
 - Resource Assignments are done at the lowest level of the WBS in Clarity PPM

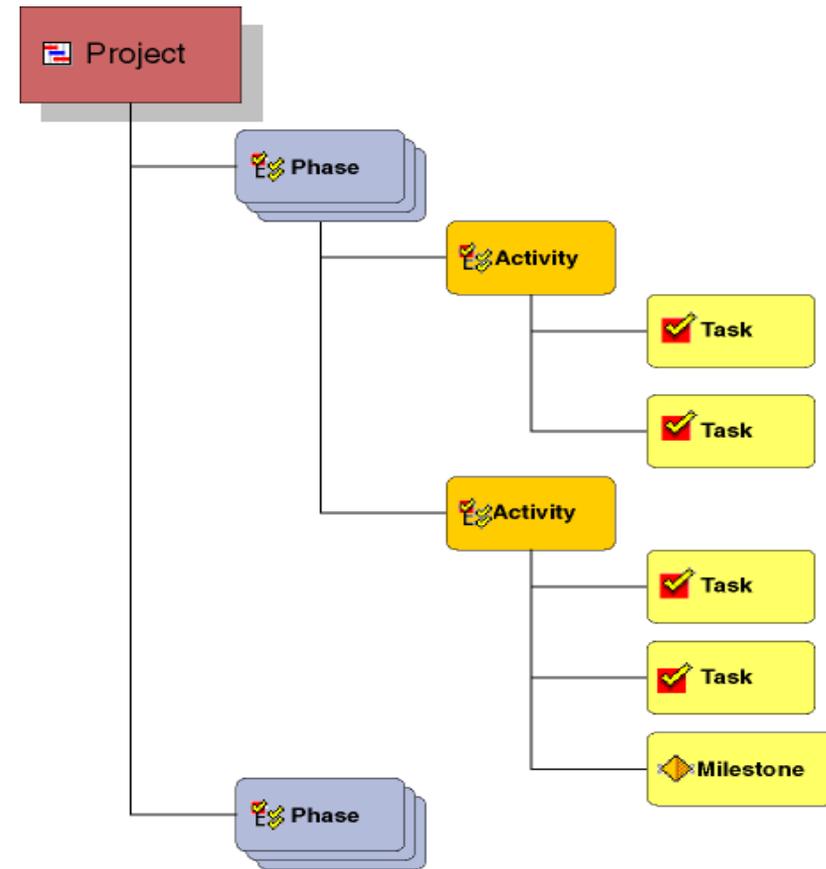

Project Management – Terms and Definitions

Term	Definition
Investment	Investments are projects, programs, applications, assets, products, ideas, services, and other work in Clarity PPM.
Organizational Breakdown Structure (OBS)	Defines hierarchical roll-ups to enable the grouping of projects by Division, Department, etc. All investments and resources in Clarity PPM are tied to an OBS.
Resource	Labor (person) and/or non-labor (expenses, equipment or materials)
Role	A generic placeholder (e.g. business analyst) used until a resource can be found to fulfill the role.
Work Breakdown Structure (WBS)	A hierarchical definition of the tasks and activities of a project that normally begins with the highest-level activities and works downward into the individual tasks and components.
Estimate to Complete (ETC)	Hours of work required for a resource to complete a task. Each resource on a task may have a different ETC. The Task ETC is the total hours for all resources to complete the task.
Scheduling Tools	Aid in refining a project's WBS, dependencies, assignment of resources and ETCs. (Open Workbench or MS Project)

Roles and Responsibilities

Project Managers

- Identify resource needs to support work demand.
- Ensure that Resource Manager approves amount of resource's time needed.
- Provide a rolling forecast of resource needs.
- Perform timely reviews of resource needs versus allocations.
- Communicate resource changes/issues/risks with Booking Manager and/or Resource Manager.



Resource Managers

- Manage resources' project and non-project allocations.
- Approve project allocations (hard book)
- Perform regular reviews of resource allocation.
- Approve Timesheets.
- Communicate resource changes/issues/risks with PMs.

Note: These activities and processes may occur both within and external to the CA PPM system, and responsibilities of each party may differ per the organization's business rules.

Modern UX and Classic

Modern

- Easy to use GUI
- Use Custom Objects
- Field Level Security
- Autosave
- Easy configurations via Blueprints
- Collaborative To Dos widget
- Staffing Plan page allows for resource analysis in grid



Classic

- Security setup
- Custom Object Creation
- OOTB Investments Module

Demo Modern UX Project Management



Let Rego be your guide.

Project Tiles View

The screenshot displays the Clarity PPM interface with a sidebar on the left and a main content area. The main area features a search bar for project managers (Dana Lewis) and a grid of six project tiles. Each tile includes a project name, ID, status, a progress bar with milestones, and three circular gauges for Next Milestone, Budget Remaining, and Effort Remaining.

Project Name	Project ID	Status	Next Milestone	Budget Remaining	Effort Remaining
AARD Payments Module	PR1151	ON TRACK	AUG 30	93.1%	74.5%
Eclipse Enhancements	PR1146	NEEDS HELP	JUL 09	78.6%	11.2%
Friday Afternoon Project	PR1175	NEEDS HELP	AUG 15	0%	100%
International Trade Show	PR1128	NEEDS HELP	-	-	-
Machine Learning Initiative	PR1154	NEEDS HELP	-	-	-
Minimal Online Shopping Site	PRS1012	ON TRACK	-	-	-

Project Grid View (1)

Clarity PPM This links to the Tiles View Projects


NEW FROM TEMPLATE

VIEW UNSAVED IT Master View

Group By

*Name ↑	*ID	Manager	*Start	*Finish	Planned Capital Cost	Planned Cost	Planned Operating Cost
AC Core Digital Rollout (Used for Roadmaps Class)	PR1231	Garvey, Sara	Jan 01 2020	Dec 31 2020	87,654	142,654	55,000
Airport Access Security (Used for Roadmaps Class)	PR1232	Garvey, Sara	Jan 29 2020	Sep 01 2020	500,000	2,000,000	1,500,000
Client Services Datamart (Used for Roadmaps Class)	PR1233	Garvey, Sara	May 15 2020	May 26 2020	25,000	47,000	22,000
CRM Enhancements (Used for Roadmaps Class)	PR1234	Garvey, Sara	Apr 05 2020	Jul 09 2020	412,000	612,000	200,000
Maintain legacy purchasing system (Used for Roadmaps Class)	PR1236	Garvey, Sara	Sep 01 2020	May 26 2021	90,000	100,000	10,000
Mobile Advertising (Used for Roadmaps Class)	PR1237	Garvey, Sara	Aug 22 2020	Jan 14 2021	125,000	145,000	20,000
Mobile Time and Approvals (Used for Roadmaps Class)	PR1238	Garvey, Sara	Dec 01 2019	May 20 2020	300,000	500,000	200,000
Online to Offline Market (Used for Roadmaps Class)	PR1239	Garvey, Sara	May 19 2020	Jul 26 2021	55,123	120,147	65,024
Security Compliance (Used for Roadmaps Class)	PR1240	Garvey, Sara	Feb 15 2020	Jul 20 2020	200,800	600,800	400,000
Web Based Trading (Used for Roadmaps Class)	PR1241	Garvey, Sara	Jul 28 2020	Oct 18 2021	12,800	39,520	26,720

Custom Investments

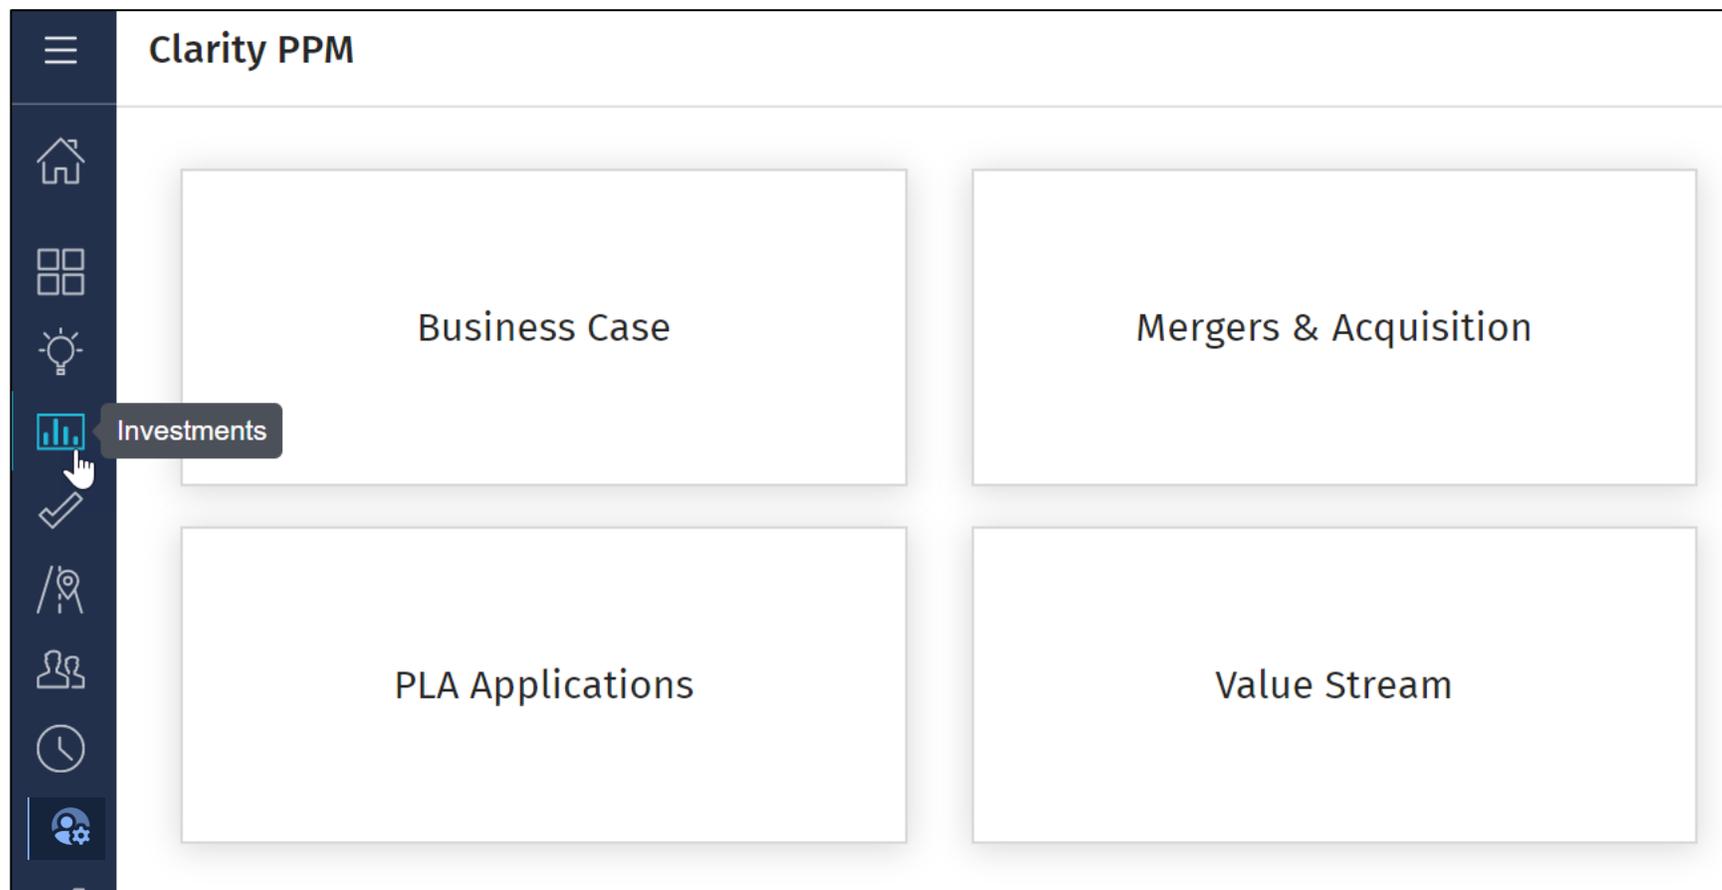

The investments list will take you to a list view as well as a Kanban-like experience. This configurable list of project type boxes will pre-filter your projects by that type.

Details Tab

- The Details tab displays the project attributes.
- Details tabs can display different data in different Blueprints.

The screenshot displays the Clarity PPM interface for the 'AARD Payments Module' project (PR1151). The project is marked as 'ON TRACK'. The 'DETAILS' tab is selected, and a red box labeled 'Milestone Status Bar' points to the 'DETAILS' tab. The project summary includes the following information:

PROJECT NAME *	PROJECT ID	SCHEDULER FORMAT	WORK STATUS
AARD Payments Module	PR1151	Microsoft Project	Requested
START *	FINISH *	% COMPLETE	PROJECT TYPE
Feb 18 2019	Aug 30 2019	0%	Major Project
DEPARTMENT OBS		STATUS REPORTING	
Corporate > IT > Business Operations		Not Required	
OBJECTIVE			

Staff Tab

- Beginning in 15.8.1, a new Add Staff button can be used to add resources, roles and teams to an investment in Clarity
- Beginning in 15.9.2, Mixed Bookings can be used on the Staffing page.

Original method for adding staff remains

New "Add Staff" button & menu introduced

Staff module within Projects, Ideas, and CITs

*Resou	Staff OBS Unit	Default Allocation	R	2020-01	2020-01
				Allocations	Allocat
Amos, Cheryl	Marketing	80.00%	E	18.40	
Awad, Rashid	Engineering	100.00%	E	23.00	
Berks, Paul	BU Staff	100.00%	P	23.00	
Berry, Jason	BU Staff	100.00%	E	0.00	
Bhatt, Rakesh	BU Staff	100.00%	E	0.00	
Garcia, Ale	BU Staff	20.00%	ML Engineer	Employee	0.00
Granger, F	BU Staff	20.00%	Project Manager	Employee	0.00
Grant, Lily	Management	100.00%	Project Manager	Employee	0.00
Lewis, Dar	Engineering	100.00%	Engineer	Employee	0.00
Morris, Tom	Engineering	100.00%	Architect	Employee	0.00

Project Task List and Tasks Tabs

• Task List

- Conversational approach
- Shows “indents” of tasks
- Easy Access to Classic Gantt, Open Workbench, and MSP

The screenshot shows the 'TASK LIST' tab in a software interface. At the top, there are navigation tabs: 'STATUS', 'ASSIGNMENTS', 'TASK LIST' (selected), 'TASKS', 'RISKS', 'ISSUES', and 'CHANGES'. Below the tabs is a search bar labeled 'Search or filter...'. The main area displays a list of tasks, each with a progress bar and a date. The tasks are:

- on Phase**: Progress bar from 0 to 100, date 'Jan 14 - Jan 14'.
- Initiating Process Complete**: Progress bar from 0 to 100, date 'Jan 14'.
- ig Phase**: Progress bar from 268 to 736, date 'Jan 14 - Aug 21'.
- ne Scope Change and Control Process**: Progress bar from 0 to 100, date 'Jan 14'.
- el Expense**: Progress bar from 0 to 100, date 'Jan 15'.
- ple task**: Progress bar from 0 to 100, date 'Aug 13'.

• Tasks

- Similar treatment as in Roadmaps
- Allows for group-bys
- Supports board, timeline and grid capabilities

Group By						
Phase Name	*Name	*Start ↑	*Finish	Status	Task Owner	Milestone
Planning Phase	Risk Response and Mitigati...	Jan 30 2019	Feb 08 2019	Started	Rubio, Sam	
Planning Phase	Identify Storage Requirem...	Feb 11 2019	Feb 22 2019	Not Started	Fowler, Ray	
Planning Phase	Identify Infrastructure Req...	Feb 25 2019	Mar 08 2019	Started	Cooper, Andy	
Planning Phase	Complete Project Plan	Mar 11 2019	May 31 2019	Started	Martin, Paul	
Planning Phase	Planning Phase Gate Comp...	Mar 22 2019	Mar 22 2019	Not Started	Martin, Paul	✓
	Design Phase	Mar 25 2019	Aug 13 2019	Started		
Design Phase	Requirements Definition	Mar 25 2019	Jun 17 2019	Not Started	Davis, Drew	
Design Phase	Hardware Acquisition	Apr 01 2019	Jun 18 2019	Started	Carmen, Ed	
Design Phase	Design Phase Gate Complete	Jun 18 2019	Jun 18 2019	Not Started	Fowler, Ray	✓
Design Phase	example	Jun 26 2019	Jun 26 2019	Completed		
	Construction Phase	Jul 09 2019	Sep 06 2019	Not Started		
Construction ...	Database Development	Jul 09 2019	Jul 22 2019	Not Started	Durand, Diane	

The Assignments Tab

Group By things like Resources, tasks, phases or other values you have displayed

ON TRACK

DETAILS STATUS ASSIGNMENTS TASK LIST TASKS RISKS ISSUES CHANGES

VIEW UNS

Standa

Group By

				Totals	2019-01	2019-02	2019-03
*Task	*Resource	*Start ↑	*Finish	ETC	ETC	ETC	ETC
Define Scope Change and...	Martin, Paul	Jan 14 2019	Jan 14 2019	0	0	0	0
Define Scope Change and...	Newburg, Mary	Jan 01 2019	May 31 2019	57	5	100	200
Travel Expense	Travel	Jan 15 2019	Jan 15 2019	12,000	12,000	0	0
Define Resource Plan	Martin, Paul	Jan 16 2019	Sep 30 2019	9	0	0	0
Risk Response and Mitig...	Morris, Tom	Jan 30 2019	Sep 30 2019	17	0	14	20
Risk Response and Mitig...	Kingsley, Art	Jan 01 2019	Sep 30 2019	995	995	995	995

The Financials Tab

- Create and edit Cost and Budget Plans

Clarity PPM Camelot Beacons Of Knowledge Platform
PR000676

[←](#)
[ASSIGNMENTS](#)
[SUB-PROJECTS](#)
[STATUS REPORT](#)
[ISSUES](#)
[RISKS](#)
[FINANCIALS](#)
[LINKS](#)

Sample Plan PLAN OF RECORD ⋮

Group By

		NOV 1, 2015-NOV	DEC 1, 2015-DEC	JAN FY 2016
		PLANNED	PLANNED	PLANNED
+	Cost T... ↑	0	0	0
	Capital	0	0	0
	Transact...			
	Contractor			

The Status Tab and Status Report Tabs

- Status Tab

- Customizable New UX Status Report
- Choose which sections to display

Clarity PPM Camelot Beacons Of Knowledge Platform PR000676

ON TRACK Hi, Sara

STATUS REPORT STATUS RISKS FINANCIALS LINKS CONVERSATIONS ISSUES DOCUMENTS

Current Reports

OVERALL STATUS Needs Help SCHEDULE STATUS On Track SCOPE STATUS Needs Help

STATUS REPORT UPDATE KEY ACCOMPLISHMENTS

REPORT STATUS Draft REPORT DATE Sep 12 2019

EFFORT METRICS Total Effort 226.40 COST METRICS Total Project Budget

Customize Status Report

INCLUDE THESE ITEMS IN STATUS REPORT

- Affected by External Factors
- Changes
- Completed Tasks
- Cost and Effort Explanation
- Cost and Effort Status
- Cost Metrics
- Created Date
- Current Phase
- Deliverable Scope Changed
- Effort Metrics
- High Level Status Module
- Objective Changed
- Overall Status
- Report Date
- Report Status
- Review Approval Problems
- Risks
- Schedule Explanation
- Schedule Status
- Scope Change Required
- Scope Explanation
- Scope Status

- Status Report Tab

- Classic Style Status Report
- Grid View Only

DETAILS TASKS STAFF ASSIGNMENTS SUB-PROJECTS STATUS REPORT STATUS RISKS FINANCIALS

Group By

*Name	Report Date	Report Status	Schedule Status	Scope Status ↑	Cost And Effort Status
Status Report_2019-09-12 15:02:43	Sep 12 2019	Draft	On Track	Needs Help	On Track

Risks, Issues, Changes Tabs

- Risks, Issues, and Changes are all available and their pages can be configured on the fly, exported to CSV files, grouped, filters, and sorted as needed.
- List View Only
- Utilize Saved views

The screenshot displays a software interface with a navigation bar at the top containing tabs: DETAILS, STATUS, ASSIGNMENTS, TASK LIST, TASKS, RISKS (active), ISSUES, CHANGES, and CONVERSATIONS. Below the navigation bar is a toolbar with a download icon, a filter icon, and a settings icon. The main area shows a table with columns: *Name ↑, Category T..., *Priority, Probability, Impact, Calculated ..., and Is Above Th. The table contains three rows: 'No budget' (Low priority, Low probability, Low impact), 'Scope Change' (Medium priority, High probability, Medium impact), and 'Sponsorship Risk' (Medium priority, Medium probability, Medium impact). A configuration panel on the right is open, showing fields for NAME * (Scope Change), CATEGORY TYPE (Implementation), and PRIORITY * (Medium). A 'CONFIGURE' button is visible in the top right of the panel.

*Name ↑	Category T...	*Priority	Probability	Impact	Calculated ...	Is Above Th.
No budget	Funding	Low	Low	Low	Low	✓
Scope Change	Implementati...	Medium	High	Medium	High	✓
Sponsorship Risk	Sponsorship	Medium	Medium	Medium	Medium	✓

Conversations Tab

- Conversations can bring the team together. This page allows for in-project chats and documents can be included.

The screenshot shows a web interface for a project management tool. At the top, a navigation bar contains several tabs: DETAILS, STATUS, ASSIGNMENTS, TASK LIST, TASKS, RISKS, ISSUES, CHANGES, and CONVERSATIONS. The CONVERSATIONS tab is currently selected and highlighted in purple. Below the navigation bar, the main content area is split into two columns. The left column displays a chat conversation. It starts with a placeholder "Start a conversation..." and a refresh icon. The first message is from Paul, dated Jan 10, 2019 5:52 pm, with a "Team" tag and mentions Dana Lewis. The second message is from Dana, dated Feb 25, 2019 9:00 pm, with a "Paul Martin" tag. A "Reply..." input field is visible at the bottom of the chat. The right column is titled "STAFF" and contains a search bar with the text "ADD Search...". Below the search bar, there is a grid of 14 staff members, each represented by a circular profile picture and a name tag. The staff members are: BENJAMIN (BA), CHERYL, JOYCE (JB), PAUL (PB), MARK (MG), WAYNE (WH), ART (AK), DANA, PAUL, TOM, MARY (MN), SANJAY (SP), and BT (BT). The text "1-14 of 14" is displayed in the top right corner of the staff list.

Documents Tab

- Documents - can be stored, organized and searched for a specific project

The screenshot shows a software interface with a navigation bar at the top containing icons and labels for 'FILE PERFORM...', 'AGILE CENTRAL', 'RISKS', 'ISSUES', 'CHANGES', 'CONVERSATIONS', 'STAFF', 'STATUS', and 'DOCUMENTS'. The 'DOCUMENTS' tab is selected and highlighted. Below the navigation bar, there is a 'Documents' section with a search bar labeled 'Search Documents' and icons for upload and add. A table below the search bar lists documents with columns for 'NAME', 'OWNER', 'MODIFIED', and 'SIZE TAGS'. One document is listed: 'Docs go here' owned by 'Dana Lewis' and modified on 'Aug 2, 2019'. A vertical ellipsis menu icon is visible at the end of the row.

NAME	OWNER	MODIFIED	SIZE TAGS
Docs go here	Dana Lewis	Aug 2, 2019	

Links Tab

- Allows for the creation of Clarity and non-Clarity links.

The screenshot displays the user interface of the Camelot Beacons Of Knowledge Platform. At the top, the page title is "Camelot Beacons Of Knowledge Platform" with the identifier "PR000676". The user is identified as "Hi, Sara" with a profile icon "SG". A notification bell icon and a "NEEDS HELP" badge are also visible. The navigation menu includes "ATUS", "RISKS", "FINANCIALS", "LINKS", "CONVERSATIONS", "ISSUES", and "DOCUMENTS". The "LINKS" tab is highlighted with a red box. Below the navigation menu, there is a "GENERAL" section with an "ADD LINK" button. Two links are listed: "Rego Consulting" and "Rego University", each with a blue circular icon containing a white 'r'.

Questions?




regoUniversity 2021
VIRTUAL

Let Rego be your guide.

Thank You For Attending regoUniversity

Instructions for PMI credits

- Access your account at pmi.org
- Click on **Certifications**
- Click on **Maintain My Certification**
- Click on **Visit CCR's** button under the **Report PDU's**
- Click on **Report PDU's**
- Click on **Course or Training**
- Class Name = **regoUniversity**
- Course Number = **Session Number**
- Date Started = **Today's Date**
- Date Completed = **Today's Date**
- Hours Completed = **1 PDU per hour of class time**
- Training classes = **Technical**
- Click on **I agree** and **Submit**



Let us know how we can improve!
Don't forget to fill out the class survey.



Phone

888.813.0444



Email

info@regouniversity.com



Website

www.regouniversity.com

Appendix

Modern UX Project Management Screens



Let Rego be your guide.

Blueprints in the New UX

- Beginning in 15.9.2, Blueprints can be configured to display specific data from templates at time of creation.

The screenshot shows the Clarity application interface. At the top, the 'clarity' logo is on the left, 'Standard Project' is in the center, and a user profile 'CA Hi, Clarity' is on the right. Below the header, a navigation bar contains 'Properties', 'Visuals', 'Modules', 'Rules', and 'Create from Template' (which is underlined). A back arrow is on the far left of this bar. On the right side of the navigation bar, it says 'Published: Aug 9, 2021'. The main content area contains the following text:

Users will see this dialog when creating a new project from a template that uses this blueprint.
When this dialog is displayed to users, any required fields not prepopulated will be appended to the end of this layout if they are not already included.

The dialog itself is titled 'New Project' and contains three input fields:


- A large text input field labeled 'PROJECT NAME *'.
- A date input field labeled 'START *'.
- A date input field labeled 'FINISH *'.

On the left side of the application, there is a dark blue sidebar with various icons. The icon representing a gear or settings (the blueprint icon) is highlighted with a red square.

Accessing Projects from the Tiles View

For users with Project Management rights, this is often your home page: the project tiles. However, it is a simple click to access from other parts of the screen.

You can click on the data in the tile to go to the project or leverage the “module shortcuts” at the bottom of the tile for a shortcut to that project page,

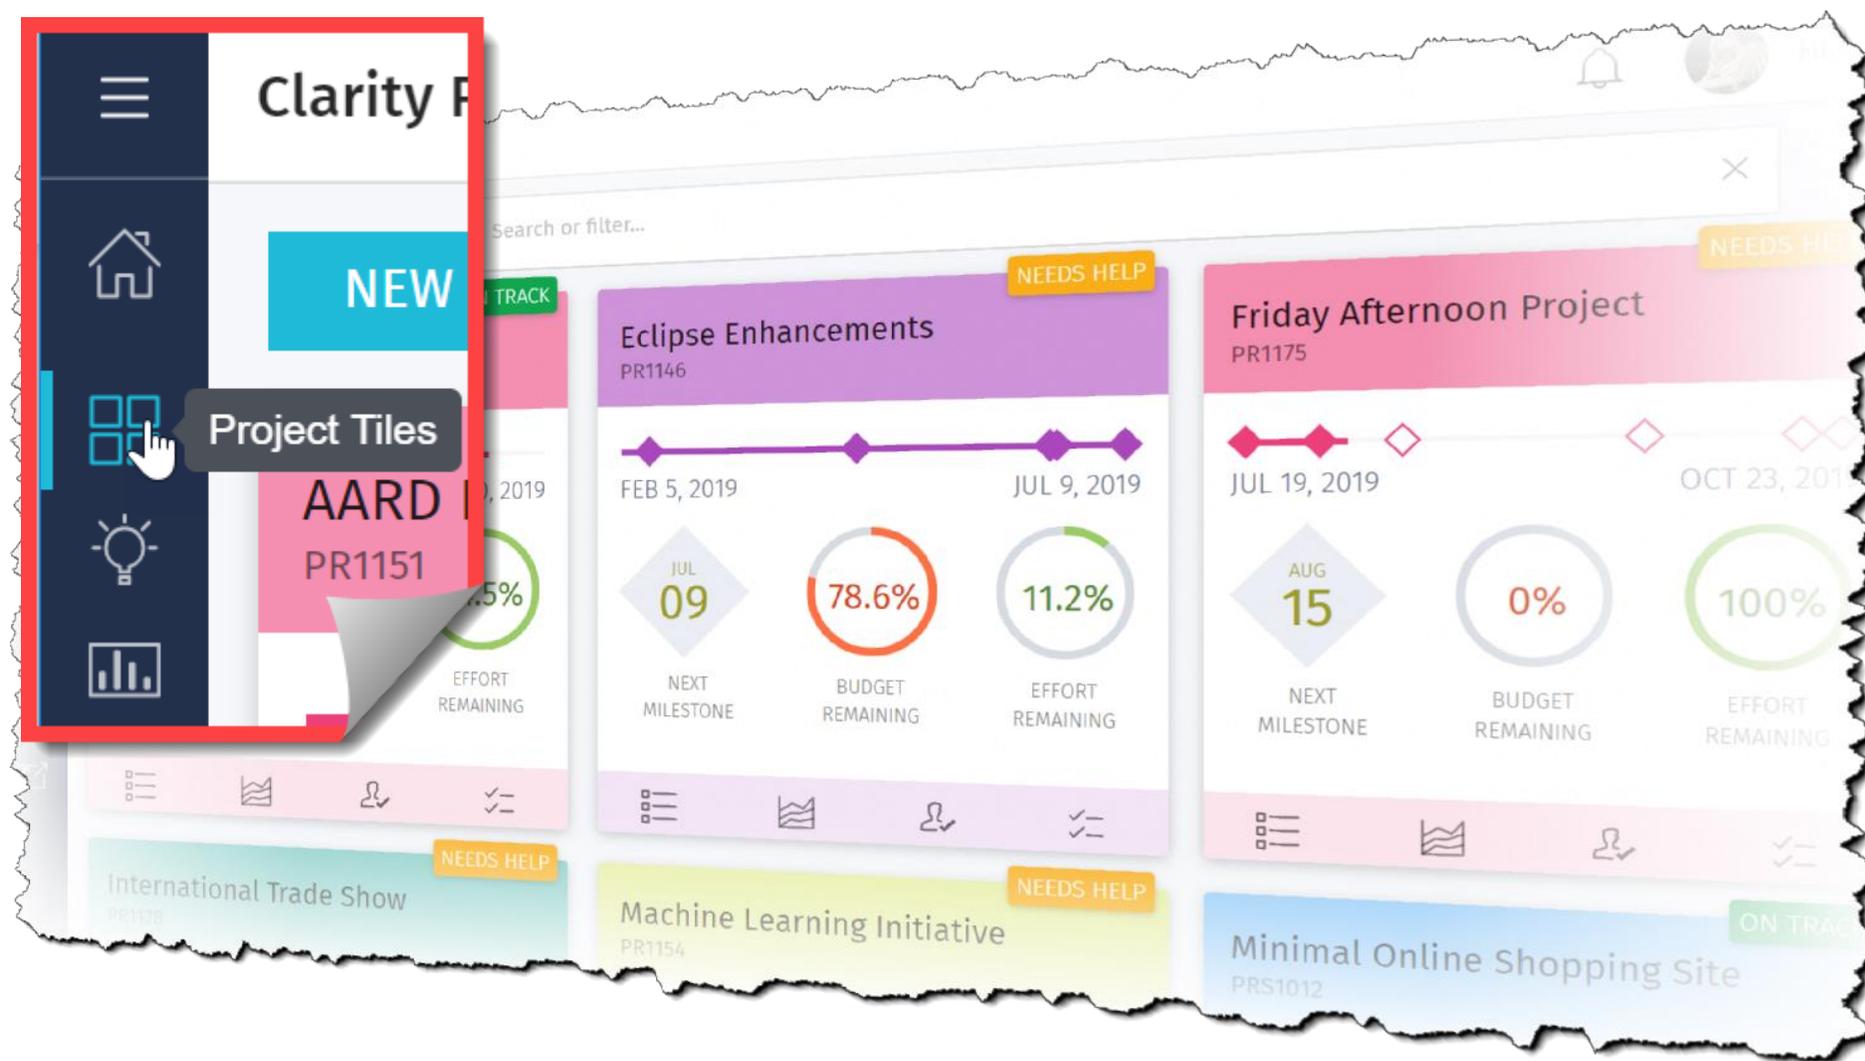

User Configurable Details Pane

- On Projects, Ideas or Custom Investments for which a user has edit rights, the user may update grid data via a configurable Details pane/panel. Users themselves may determine which fields appear on the panel, and panel configurations can be saved to a view.
- Note that you must first click on an item in the list before the Details Pane will appear.

The first screenshot shows the 'Projects' view in the 'Clarity PPM' application. A table lists various projects, and a 'DETAILS' button is highlighted in the bottom right corner of the table.

*Name ↑	Blueprint	*ID	Manager	*Start
AC Core Digital Rollout (Used for Roadmaps Class)	Standard Project v2	PR1231	Garvey, Sara	Jan 2020
Airport Access Security (Used for Roadmaps Class)	Standard Project v2	PR1232	Garvey, Sara	Jan 2020
Client Services Datamart (Used for Roadmaps Class)	Standard Project v2	PR1233	Garvey, Sara	May 2020
CRM Enhancements (Used for Roadmaps Class)	Standard Project v2	PR1234	Garvey, Sara	Apr 2020
Maintain legacy purchasing system (Used for Roadmaps Class)	Standard Project v2	PR1236	Garvey, Sara	Sep 2020
Mobile Advertising (Used for Roadmaps Class)	Standard Project v2	PR1237	Garvey, Sara	Aug 22
Mobile Time and Approvals (Used for Roadmaps Class)	Standard Project v2	PR1238	Garvey, Sara	Dec 01
Online to Offline Market (Used for Roadmaps Class)	Standard Project v2	PR1239	Garvey, Sara	May 19
Security Compliance (Used for Roadmaps Class)	Standard Project v2	PR1240	Garvey, Sara	Feb 15
Web Based Trading (Used for Roadmaps Class)	Standard Project v2	PR1241	Garvey, Sara	Jul 28

The second screenshot shows the details pane for the 'AC Core Digital Rollout' project. A 'CONFIGURE' button is highlighted in the top right corner of the details pane.

The third screenshot shows the configuration options for the details pane. A search bar is at the top, and a list of fields is shown on the right. A hand icon is pointing to the '% COMPLETE' field in the list.

Project Grid View (2)

- Beginning in 15.6.1, a new project link was made available in the Left Navigation menu that displays projects in a grid view, similar to the Project List in Classic.
- The common New UX grid view is utilized here, that allows for filtering on any project attribute, saved filters, saved views, sorting, grouping, etc.
- Security Rights are associated with each View:
 - Project Management - Tiles Navigate: Allows user access to the project management **Tiles** page in the new user experience. The user will only be able to view information for projects to which the user has access.
 - Project Management – Navigate: Allows user access to the project management (**Grid**) pages in the new user experience. The user will only be able to view information for projects to which the user has access.

The Configurable Grid View

Clarity PPM Business Case business_case

Hi, System

VIEW UNSAVED

Search...

Export to CSV

Configure the View

Pick your Columns

*Name ↑	*ID	Manager	Work Progr...	Alignment	Work Stage	*Progress	*Start	*Status	*F
Clarity Implementation	000-03	Fleming, Nicole	Not Started	12	Business Case	Started	Dec 13 2018	Approved	
klsdm'lksdmf'l	000-06	Lewis, Dana		22	Development	Not Started	Jun 13 2019	Unapproved	
Mobile API Enhancements	000-05	Administrator...		45	Demand Capt...	Not Started	Mar	Approved	Ma
Mobile Payment App commerce pla...	000-04	Lewis, Dana	Not Started	56	Business Case	Started	Dec	Approved	Dec
Network Monitoring Upgrade	000-01	Lewis, Dana	Not Started	100	Business Case	Not Started	Dec 13 2018	Unapproved	Dec
New Online Application	000-02	Lewis, Dana	Started	87	Business Case	Not Started	Dec 13 2018	Unapproved	Dec

You can configure your view and easily export to csv.

The Investment grid - Summary Details of an Investment

By selecting a single investment, you will see an additional menu appear: the Details View.

The screenshot shows a software interface with a grid of investment items and a details view for a selected item. A blue callout box highlights a 'CONFIGURE' button in the grid, with the text: "Configure the columns available in the grid view".

*Name ↑	Investment	Work Stage
Clarity Implementation		
Mobile API Enhancement		
Mobile Payment App com	12	Business
Network Monitoring Upgr	45	Demand
New Online Application	56	Business Ca
New Safety Monitoring Sy	100	Business Ca
	87	Business Ca
	22	Developme

CONFIGURE

NAME *

Network Monitoring Upgrade

INVESTMENT ID

000-01

MANAGER

Lewis, Dana

WORK PROGRESS

Not Started

WORK STAGE

Business Case

PROGRESS *

Work Stage	*Progress	*Start	*Status	*F
Business Case	Started	Dec	ed	D
demand Capt...	Not Started	Mar	ed	M
Business Case	Started	Dec	oved	D
Business Case	Not Started	Dec	oved	D
Business Case	Not Started	Dec	oved	D
development	Not Started	Jun 13 2019	Unapproved	Jun

You can see the details of your project/investment as well as configure the data points you are displaying.

Custom Subobjects and Channels

- Custom Subobjects may also be displayed as a tab within the Project.
- Channels can be used to access data in Classic, or other external systems.

Clarity PPM Camelot Beacons Of Knowledge Platform PR000676

NEEDS HELP

DETAILS TASKS STAFF ASSIGNMENTS **SUB-PROJECTS** STATUS REPORT

CLASSIC Clarity PPM

PROPERTIES TEAM TASKS RISKS/ISSUES/DECISION LOG PROCESSES DASHBOARD

Project: Covance Master Project - Properties - Subprojects [Open in Scheduler](#)

ACTIVE
Yes

FILTER SHOW ALL CLEAR

<input type="checkbox"/>	Project ▲	ID	Count	Actuals	ETC	Total Effort	Percent Expended	Baseline	Status	Schedule	Read Only
<input type="checkbox"/>	Covance Sub Project 1	PR000557	0	0	0	0		0	◆		
<input type="checkbox"/>	Covance Sub Project 2	PR000558	0	0	0	0		0			
	Total		2	0	0	0	0.00%	0	◆		

Displaying 1 - 2 of 2

ADD REMOVE SET READ-ONLY SET READ/WRITE

= Program Work Effort = Hours
